



## **WEEKLY INSPECTOR'S FORECAST**

---

November 14<sup>th</sup>, 2017

<b>FOR WEEK ENDING:</b>	November 11 <sup>th</sup> , 2017
<b>PROJECT NAME:</b>	Chicago St. Phase 3
<b>CONTRACT NUMBER:</b>	R-34740
<b>PROJECT LOCATION:</b>	Hammond, Indiana
<b>OWNER:</b>	INDOT
<b>CONTRACTOR:</b>	Rieth-Riley Construction Co., Inc.
<b>DESIGN ENGINEER:</b>	American Structurepoint
<b>PROJECT SUPERVISOR:</b>	Kevin Walsh - American Structurepoint
<b>LETTING DATE:</b>	April 5, 2017
<b>NOTICE TO PROCEED:</b>	May 5, 2017
<b>SUBSTANTIAL COMPLETION:</b>	N/A
<b>FINAL COMPLETION:</b>	August 10, 2018
<b>PERCENT OF PROJECT COMPLETE:</b>	35%

---

### ➤ **Recent Activity (Nov 6<sup>th</sup> to Nov 11<sup>th</sup>)**

- Fine graded west of Chicago/Ash intersection on Chicago St. and all approaches for sub-grade treatment.
- Sub-grade treatment (stabilization) for the south side of Chicago St between just east of Elm to Cedar Ave.
- Geo-grid and stone on the north side of Chicago St. between Ash and Cedar
- More 53 stones were places between Hickory and Ash to rise the road on top of the 36'' water main.
- Hawk installed street lighting conduits underneath driveways
- Falk implemented the new elevation changes and to establish the curb and center lines along Chicago St
- Curb String lining was set up for curb and gutter pouring
- Castings for inlets, catch basins and manholes were adjusted to the right elevation

### ➤ **Anticipated Activities for the Upcoming Week (Nov 12<sup>th</sup> to Nov 18<sup>th</sup>)**

- Falk on site to establish the curb line on the south side of Chicago St, from just east of Elm to Cedar Ave
- Paving the first lift of base on the north and south side of Chicago St. from just east of Elm to Cedar Ave
- Curb String lining will be set up for curb and gutter pouring on the south side of Chicago St

### ➤ **Of Note**

- The next progress meeting will be held on Tuesday November 14<sup>th</sup>, at 2 o'clock.

### ➤ **Personnel**

- Staffing includes one Project Supervisor, two Inspectors




Curb and Gutter Pouring



Curb and Gutter Finishing



South Side Sub-grad Treatment (Stabilization)

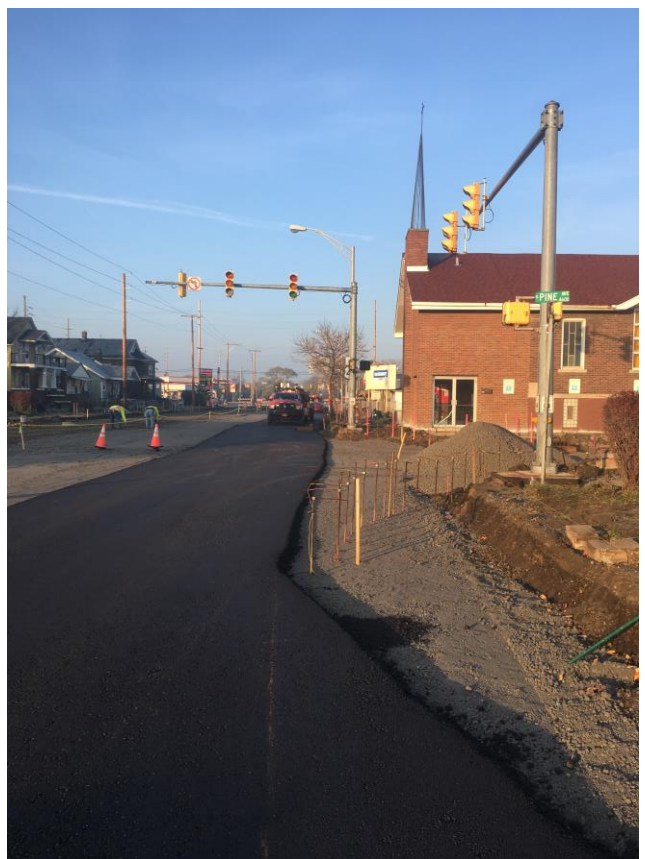

North Side First Lift of Base
